#### Salem Police Station Update

Subcommittee Meeting December 4<sup>th</sup> 2018



#### Project Status Update

- Permitting
- Subcontractor Procurement
- Construction Start
- Preparing 100% Construction Documents
- Art Selection Process
- User Group Meetings
- Budget Updates



### Permitting Activities

#### **Permit Tracking**

- ✓ Site Plan Review COMPLETE
- ✓ Early Sitework Permit COMPLETE
- Rammed Aggregate Pier Permit PENDING
- Early Foundation Permit PENDING
- Early Under Slab Utilities PENDING




Overall Onsite
Construction Valuation
\$48.7 Million

# Sub-Contracting

STATUS	ID#	DATE	DESCRIPTION	AMOUNT	TOTAL
APPROVED	Original Contract	2/27/2018	Original CM/GC Contract - Precon Services	\$173,250	\$173,250
APPROVED	Amendment #3	10/16/2018	MEP Pre-Con Services and Geo Peer Review	\$191,077	\$364,327
		Pre-Construction		\$364,327	
APPROVED	Amendment #1	9/10/2018	Insurance Terms - Adjusted	\$0	\$0
APPROVED	Amendment #2	10/17/2018	Early Work #1 - Earthwork & Utilities & GC/GR's	\$2,161,655	\$2,161,655
APPROVED	Amendment #4	11/1/2018	Early Work #2 - Structural Concrete & GC/GR's	\$8,284,593	\$10,446,248
TENTATIVE	Amendment #5	DEC 18	Early Work #3 - Precast, Elevator, Embeds, Waterproofing, UnderSlab MEP		
TENTATIVE	Amendment #6	JAN 19	Early Work #4 - System Integrator, Steel, Other Items TBD		
TENTATIVE	Amendment #7	MAR 19	Early Work #5 - Bldg Envelope & Mechanical, Electrical & Plumbing		
	Onsite GMP Amendment	APR 19	Guaranteed Maximum Price		
			Construction Subtotal	\$10,446,248	
			CM/GC CONTRACT TOTAL	\$10,810,575	

## Schedule Update

- Work Complete
  - Installation of Fence
  - Removal of Asphalt
  - Site Grading
- Upcoming Work
  - Ongoing Underground Utilities
  - Week of 12/10 Aggregate Piers
  - Week of 1/14 Foundations Begin

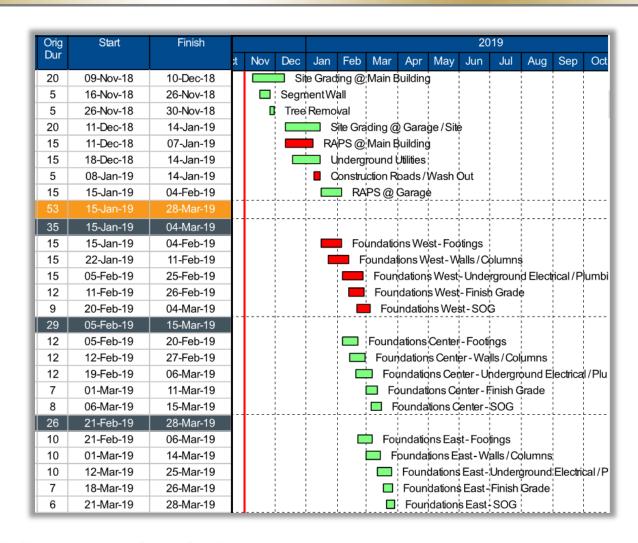

### Design Updates

- Incorporation of Drawing Comments from DD Milestone Set
- Continued User Group Meetings for Refinements
- Public Art RFP Process



Bidding & Permit Set of Final Documents (Feb/Mar 2019)










#### Project Budget – The Big Picture

#### Salem Police Station: Project Funding Summary – 104,000 SF Facility

FUNDING TYPE	OVERALL BUDGET	CONSTRUCTION BUDGET	ACTUAL CONSTRUCTION	SOFT COSTS	SOFT COST %
May 2017 Bond Amount Confirmed Cost Reductions Pending Cost Reductions	\$ 61,814,000	\$ 42,233,000	\$ 56,225,031 - \$ 4,331,789 - \$ 2,035,712	\$ 18,581,000	30.06%
Bond Premium Interest Public Works Funds Riverfront Downtown	\$ 4,222,611 \$ 1,457,564 \$ 600,000 \$ 2,085,000	\$ 2,481,966 \$ 1,457,564 \$ 600,000 \$ 2,085,000		\$ 1,740,645	
Urban Renewal Funds TOTAL	\$ 70,179,175	\$ 49,857,530	\$ 49,857,530	\$ 20,321,645	28.96%

#### Project Budget – Measuring Risk

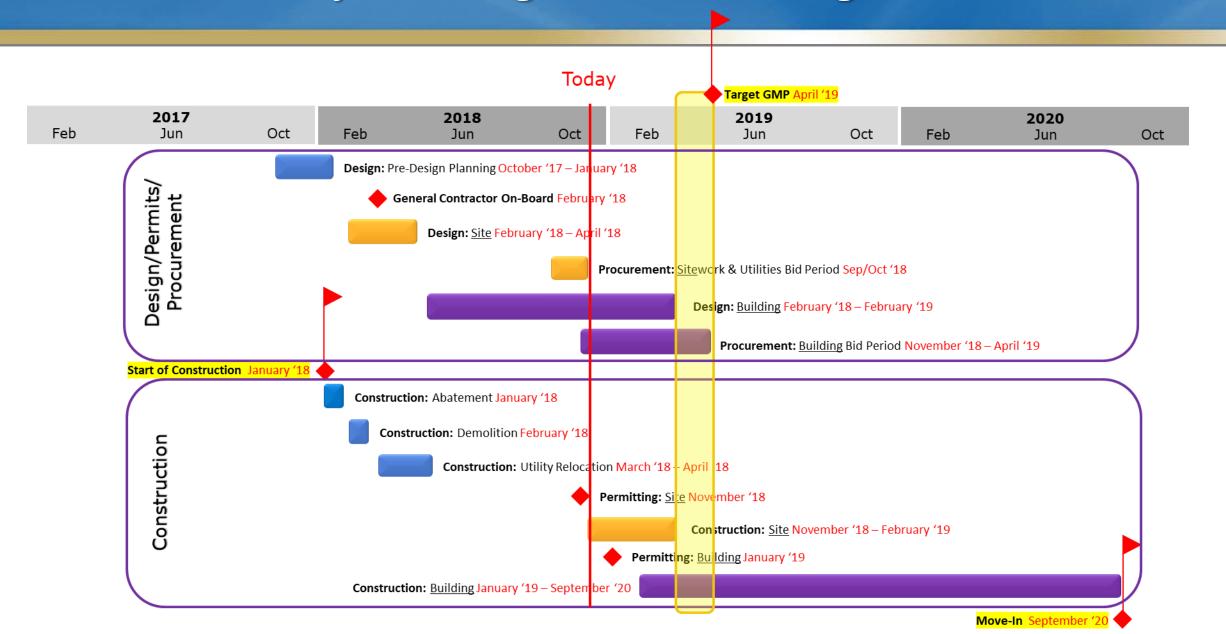

#### Project Budget – Future Subcommittee Meetings

- January 16 2019 50% Construction Documents Cost Estimate Update
- February 20 2019 Cost Update
  - Value Engineering/Options
  - Contingency
  - Bid Alternates
- March 20 2019 Present Draft Budget Numbers & Approval Path
- April 17 2019 Presentation Trial Run & Adjustments
- April 22 2019 Council Action

#### Outreach & Public Relations

- Archaeology Grant ES Student Participation
- Continued Sub-Contracting Outreach
  - Chemeketa Center for Business & Industry
  - Salem Chamber of Commerce
  - Salem Capitol Connections February 7<sup>th</sup> 2018
  - Latino Business Alliance
- CTEC Summer Internship Planning
- Ground Breaking Occurred November 9th
- Neighborhood Association Updates
- Building Buzz & Social Media Posts



#### **Next Update**

Open Discussion - Questions

Next meeting is scheduled for January 16<sup>th</sup>, 2018
