


Salem Library Improvement Project

Council Committee Meeting – March 19, 2021




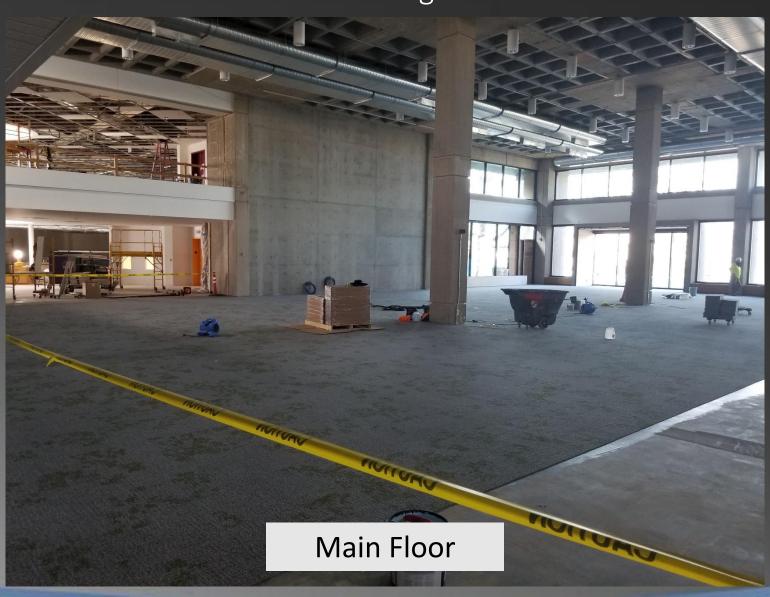


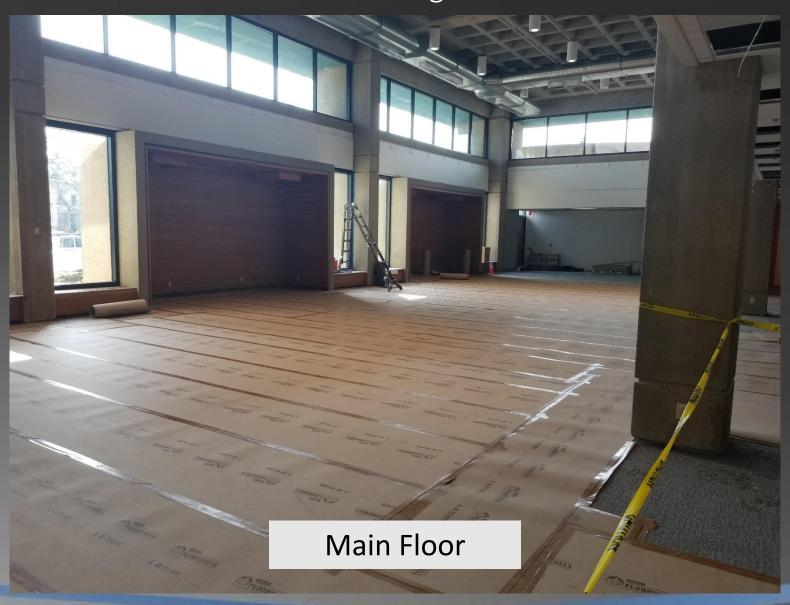

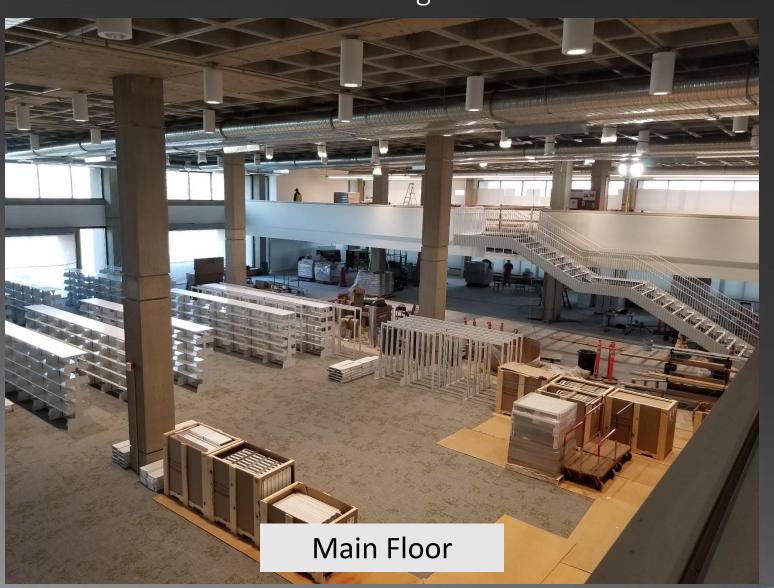




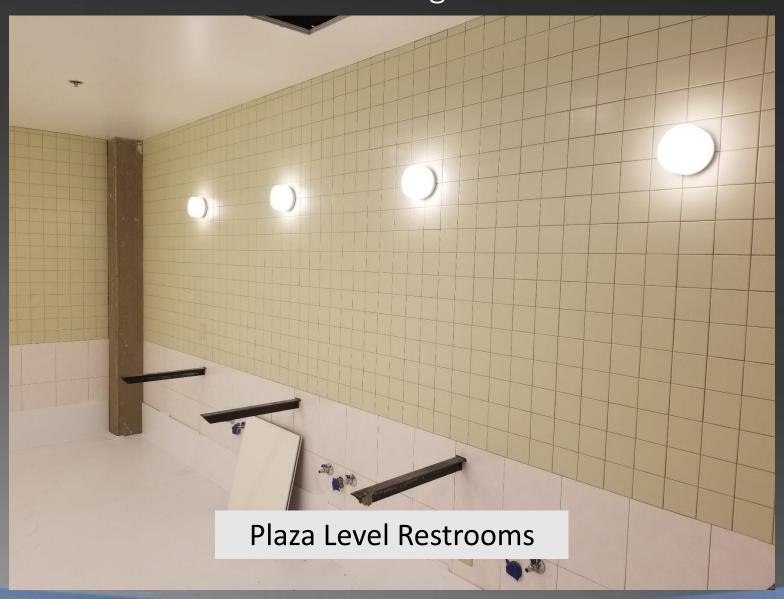

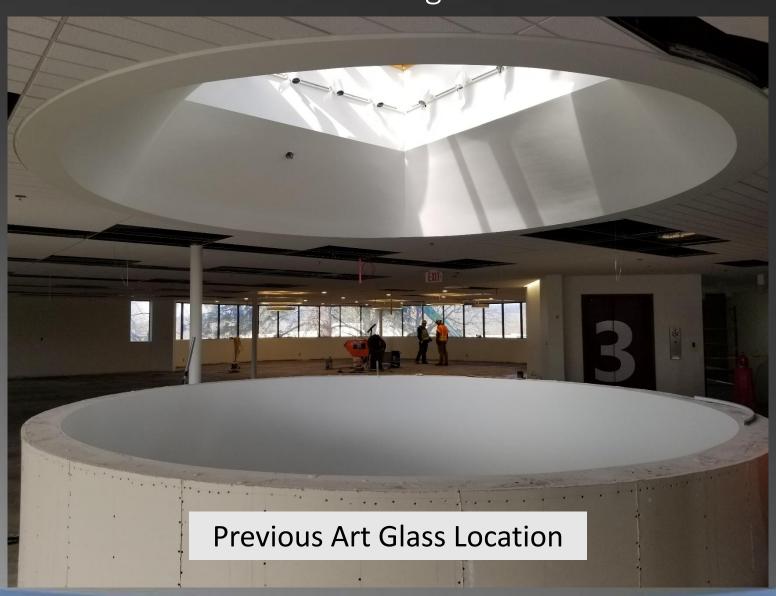

Construction Progress Photos







New Art Glass Location

HACKER

Salem Public Library Improvements Project Budget – Current Expenditures

	Budget	Expenditures (02/28/21)
DESIGN BUILD SERVICES	\$19,636,982	\$14,159,445
 Phase 1 – Schematic Design 	\$403,410	\$403,410
 Phase 2 – Final Design 	\$1,148,012	\$1,148,012
 Phase 3 – Construction 	\$17,436,514	\$12,386,893
Foundation Improvements	\$620,590	\$221,130
OWNER COSTS	\$1,906,781	\$1,311,626
CONSULTANT COSTS	\$877,208	\$657,596
OWNER CONTINGENCY	\$401,510	
TOTAL PROJECT COST	\$22,822,481	\$16,128,666

Project Budget

Owner Contingency	\$401,510
HSW Contingency (3/10/21)	\$236,188
- Projected additional spend down (including Art Glass)	(\$150,000)
ETO Incentives	\$107,750
Forecasted Available Contingency	\$591,859
Additional Scope Items	
- Added Furniture Scope	\$140,000
- Plaza Level Gate Replacement	\$35,000
- Exterior Signage	\$10,000
- Bike Racks	\$10,000
- Parking Structure Traffic Coating	\$250,000
- Unanticipated Items	\$50,000
Fund All Items	(\$495,000)
Projected Project Balance	\$96,859
